




— BUREAU OF —
RECLAMATION

Navajo-Gallup Water Supply Project



Update for NM Water and Natural Resources
Committee

July 12, 2021

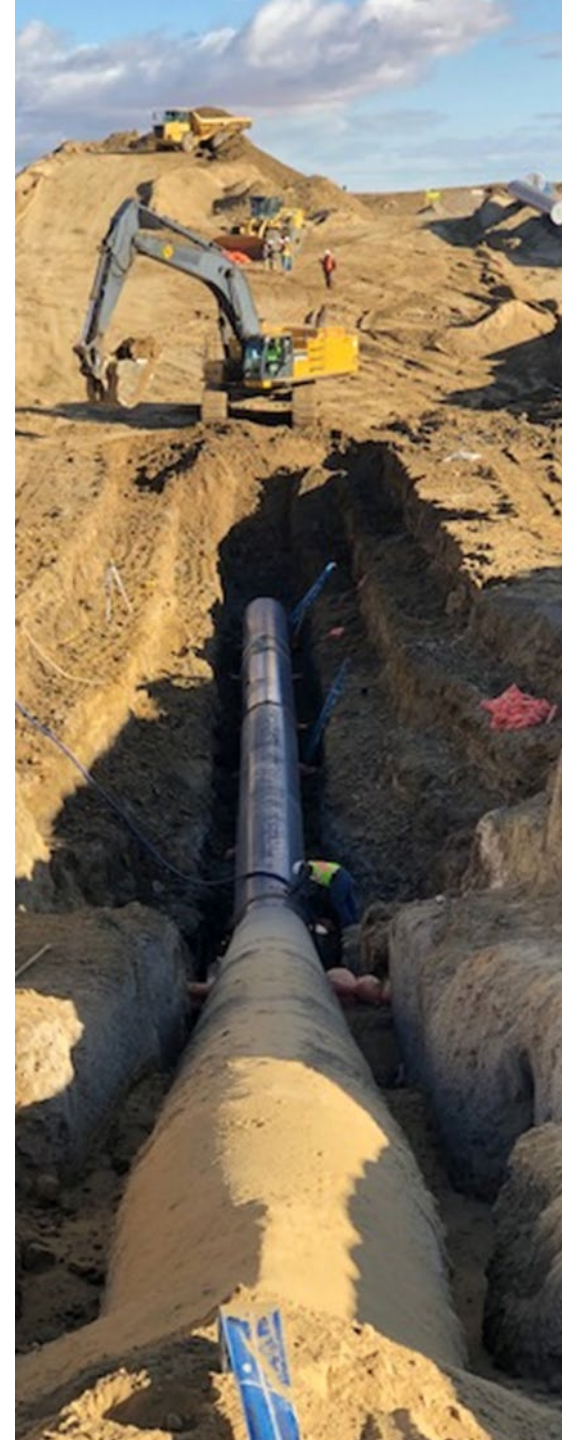

San Juan Lateral

Cutter Lateral

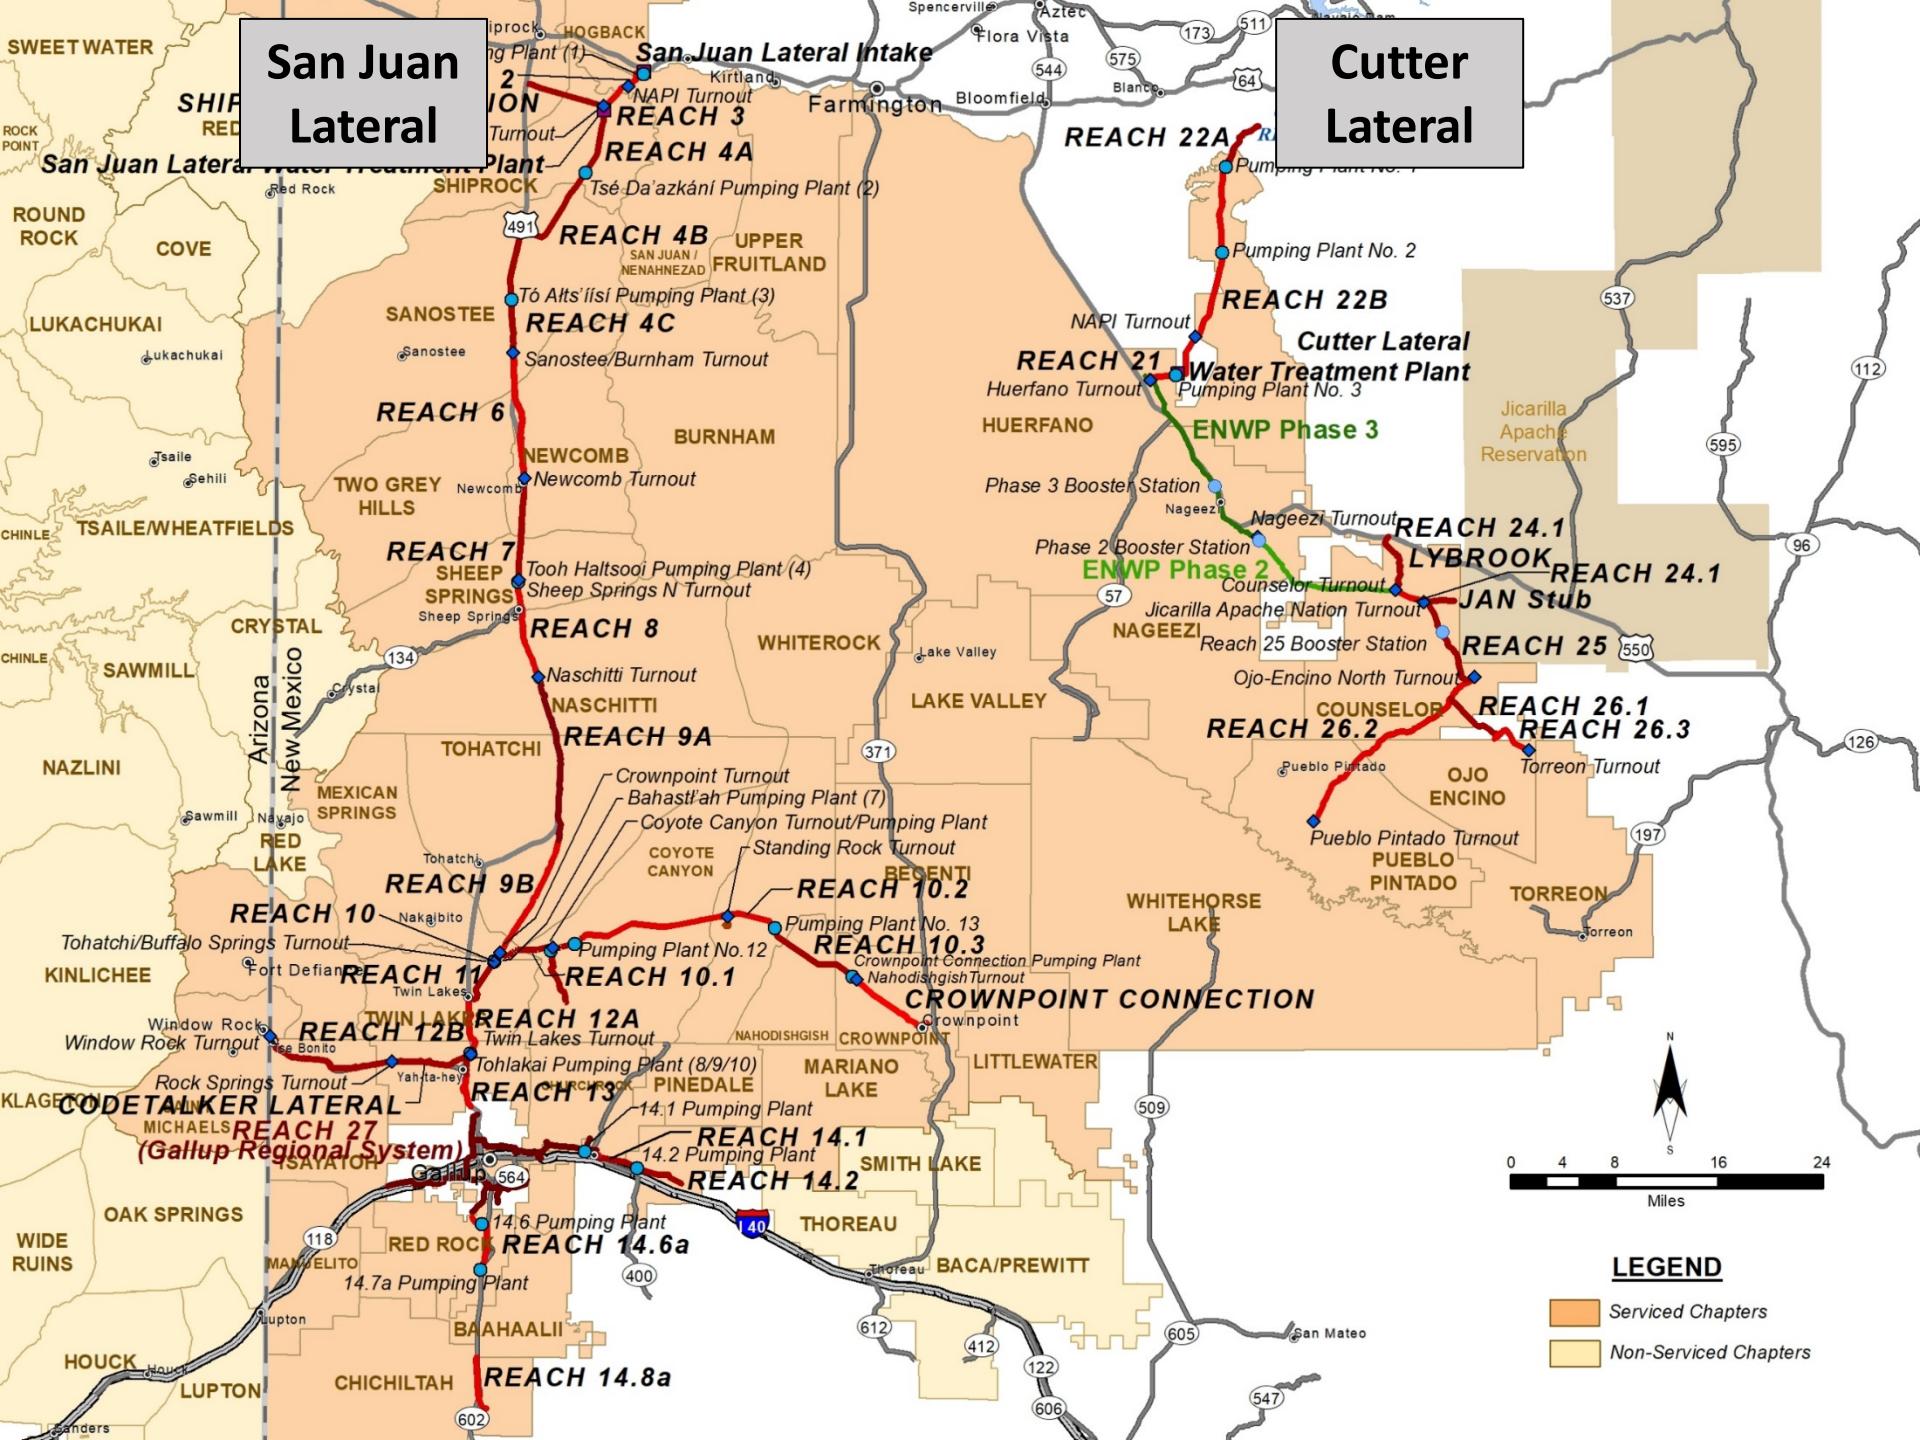

LEGEND

- Serviced Chapters
- Non-Serviced Chapters


Background

- Navajo-Gallup Water Supply Project (NGWSP) authorized by Public Law 111-11 in 2009
- Authorized \$870 million (2007 price level), indexed and tracked using the Construction Cost Estimate (CCE)
- Current Ceiling (Oct 2020 \$) = \$1,348 million
- Beneficiaries
 - Navajo Nation
 - City of Gallup
 - Jicarilla Apache Nation
- Funding Sources
- Project in heightened focus due to impact of COVID-19




San Juan Lateral

Cutter Lateral

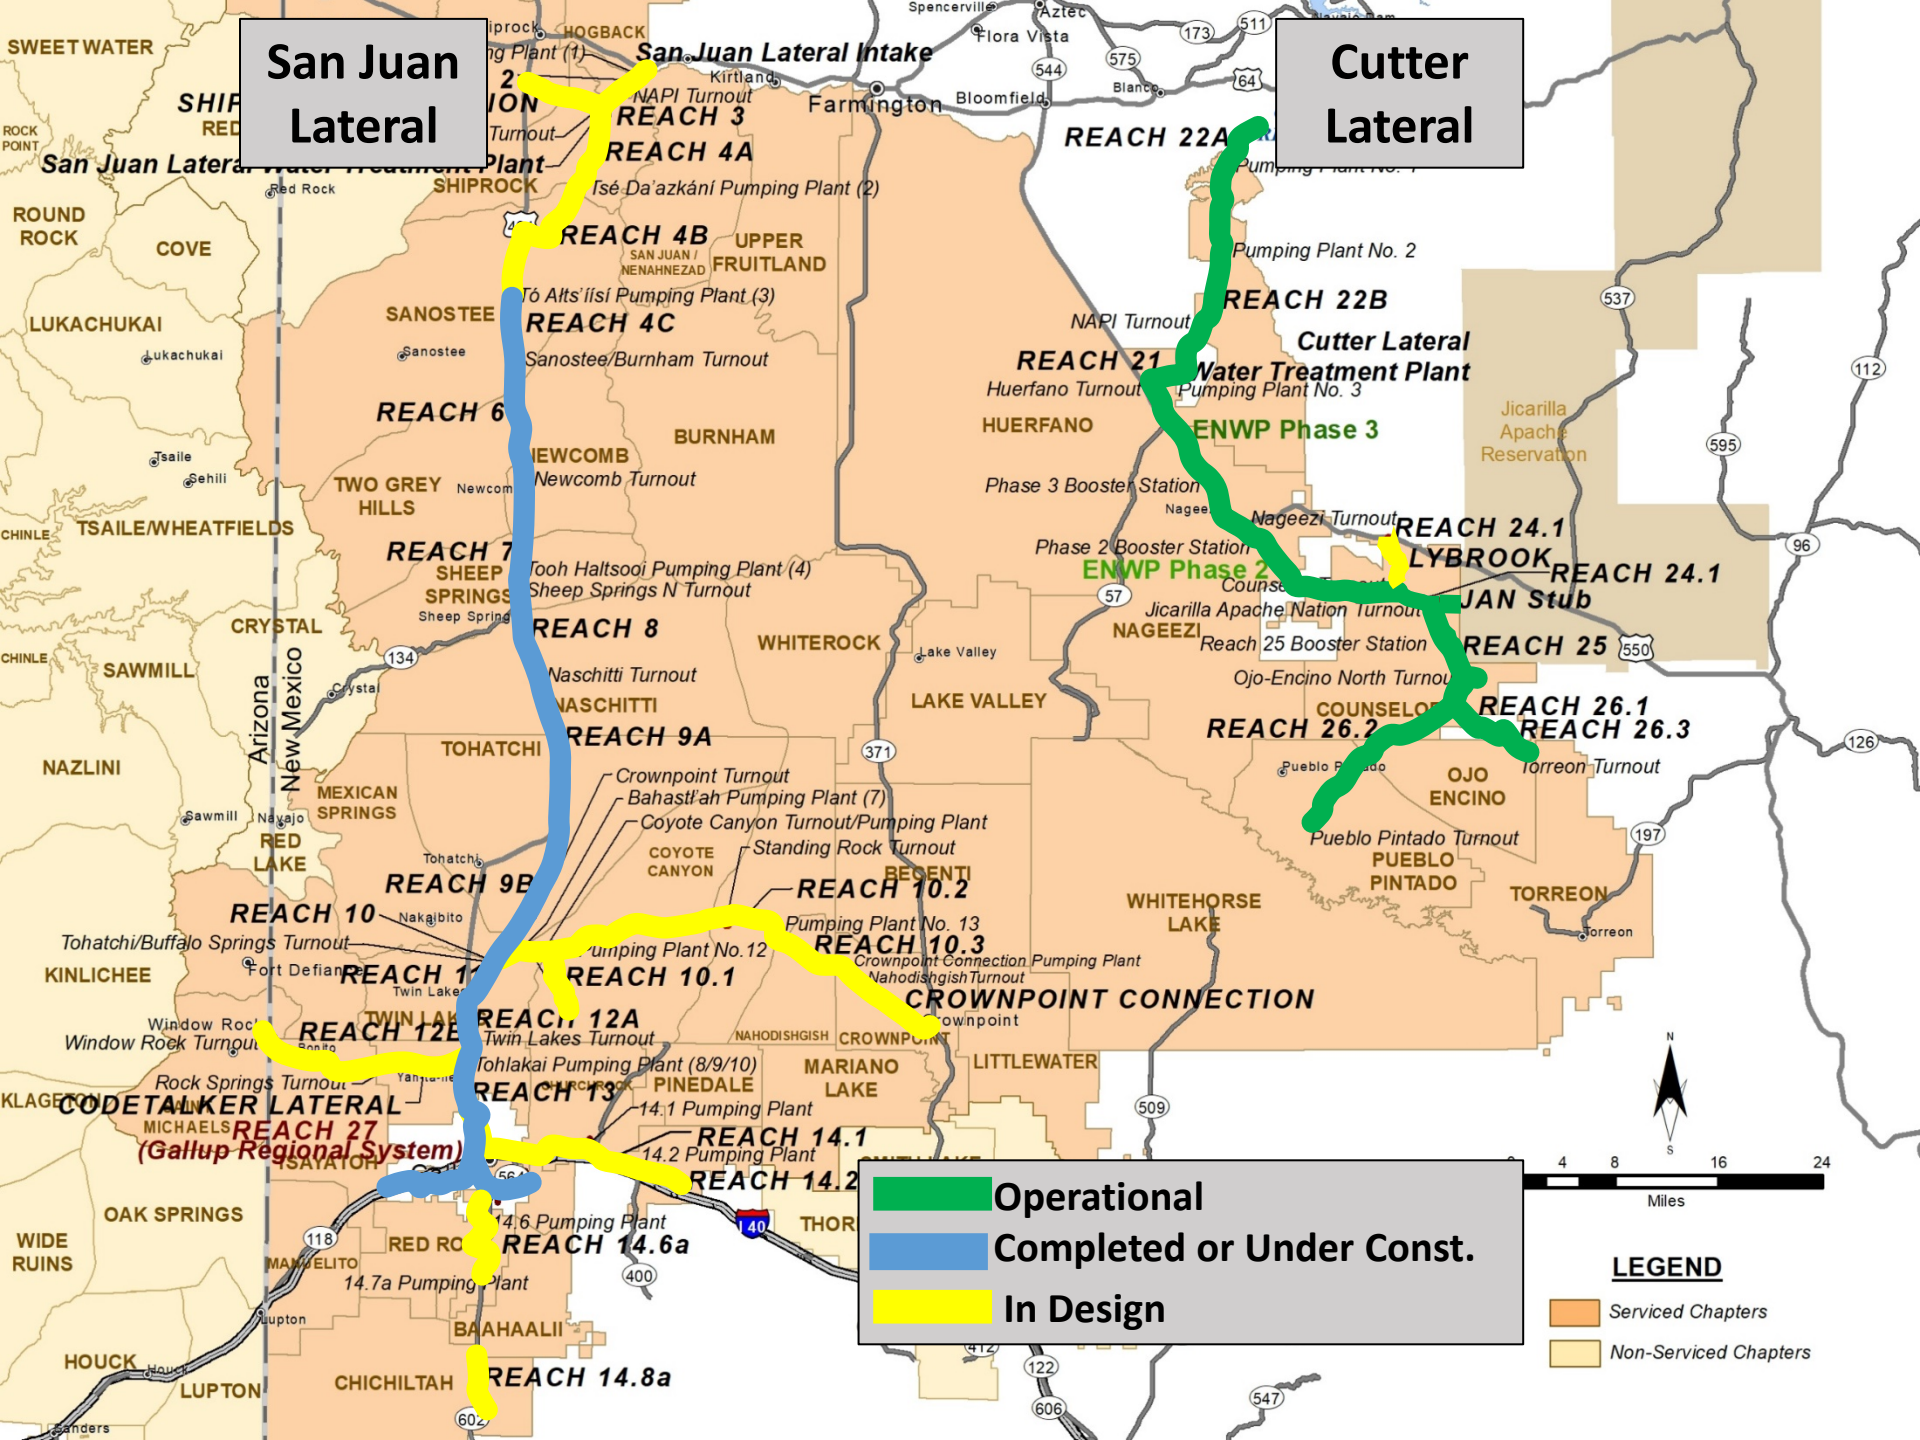

Operational
Completed or Under Const.
In Design



LEGEND

- Serviced Chapters
- Non-Serviced Chapters

Status of Project Construction


Cutter Lateral Side (eastern side):

- Construction is complete
- First water deliveries to the Cutter Lateral began in Oct 2020
- 8 Navajo communities now receiving water; Jicarilla Apache Nation to be served later this summer
- Anticipated transfer of OM&R responsibility to NTUA in Fall 2021



Cutter Lateral Water Treatment Plant




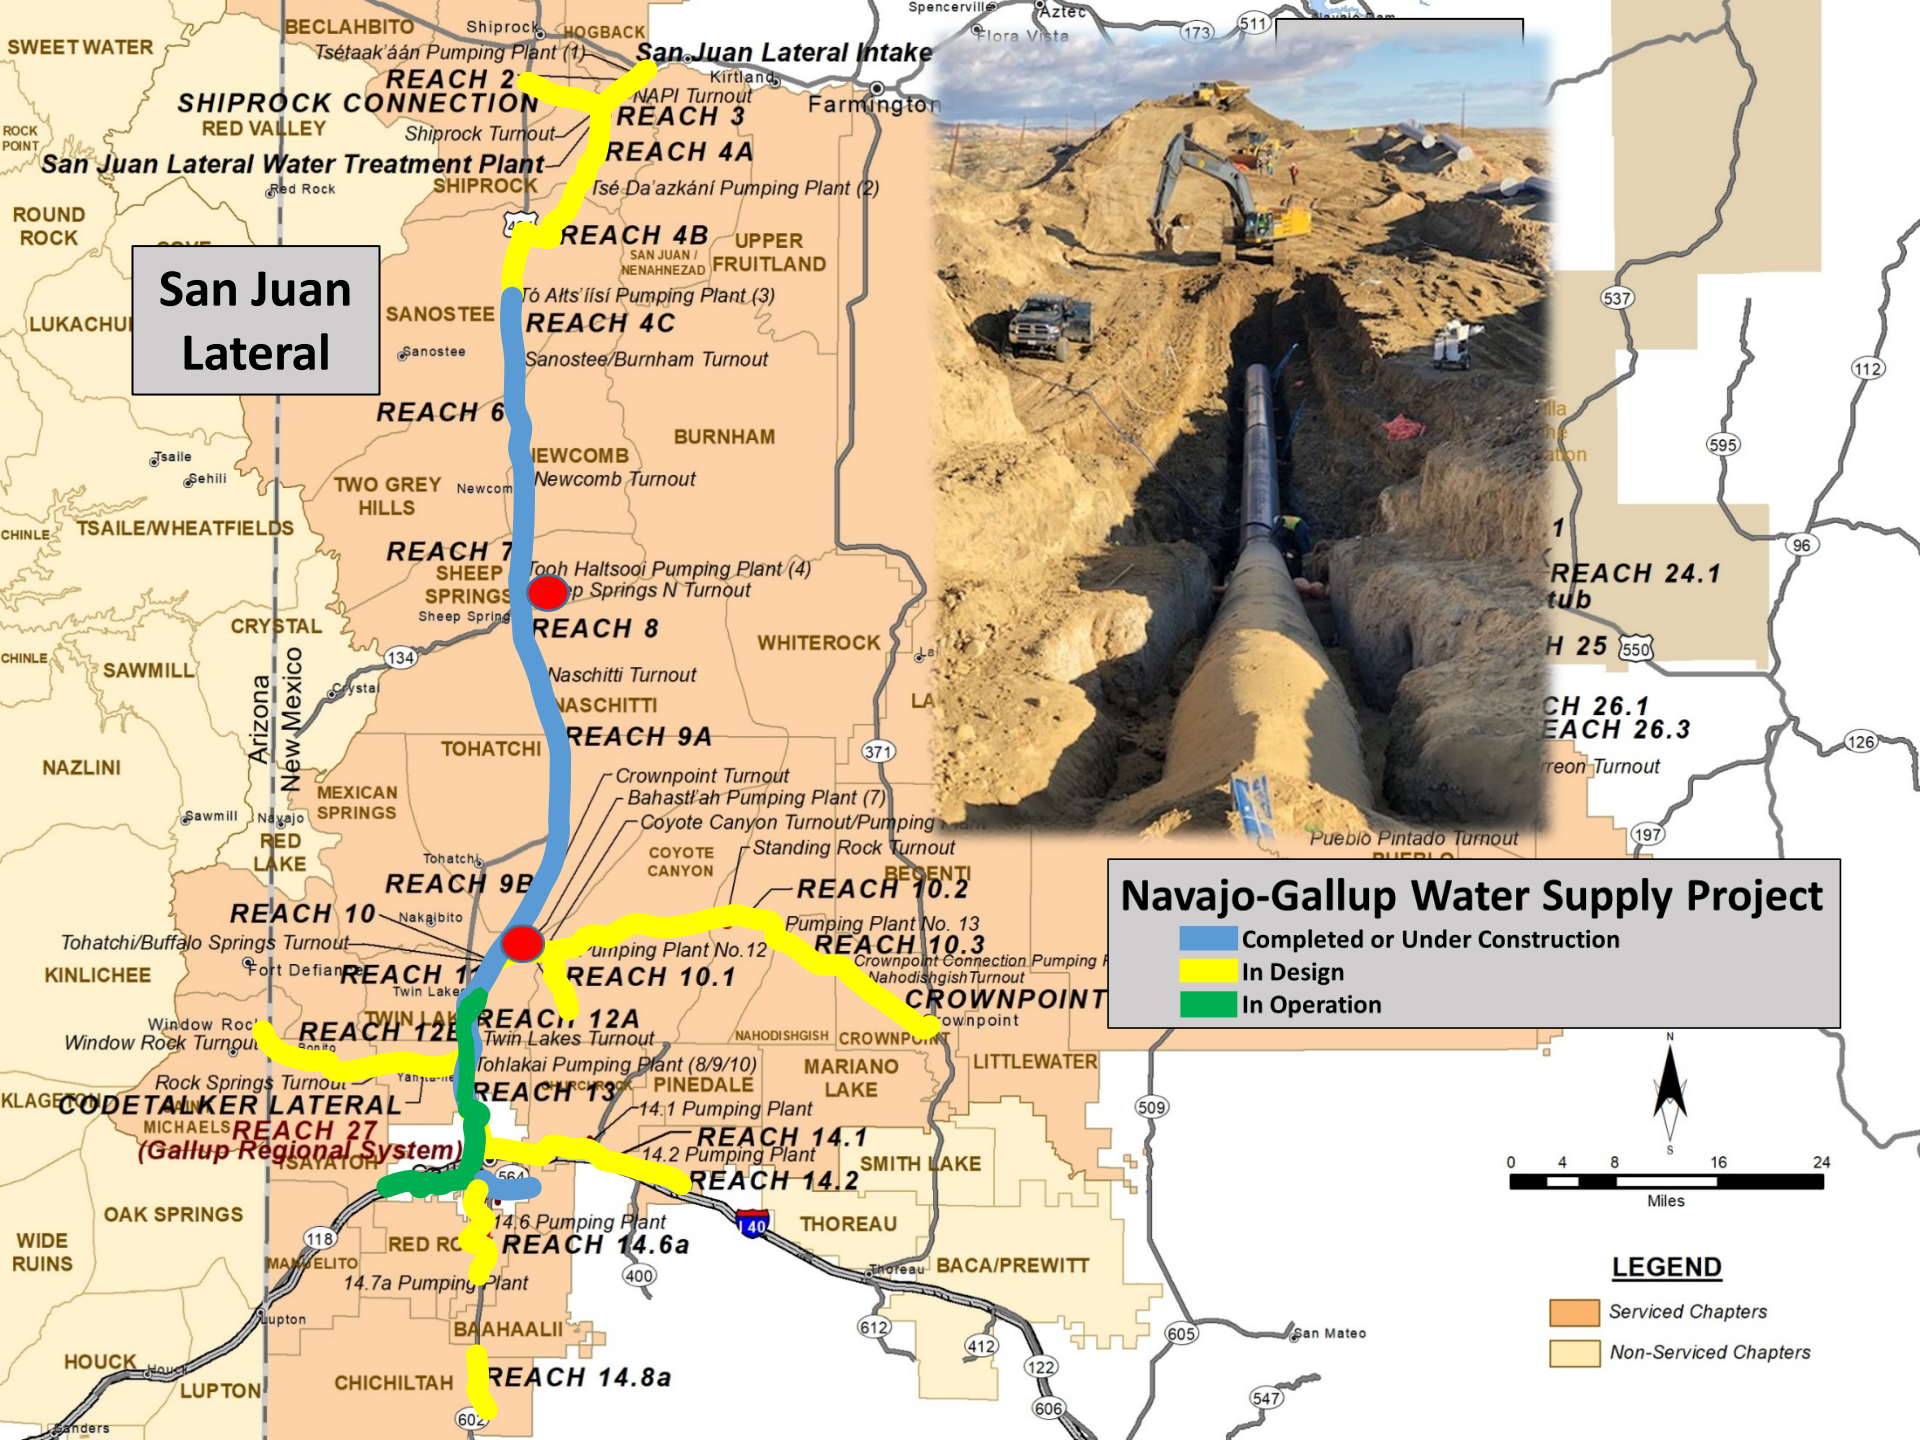


San Juan Lateral

Navajo-Gallup Water Supply Project

- █ Completed or Under Construction
- █ In Design
- █ In Operation



- LEGEND**
- Serviced Chapters
 - Non-Serviced Chapters

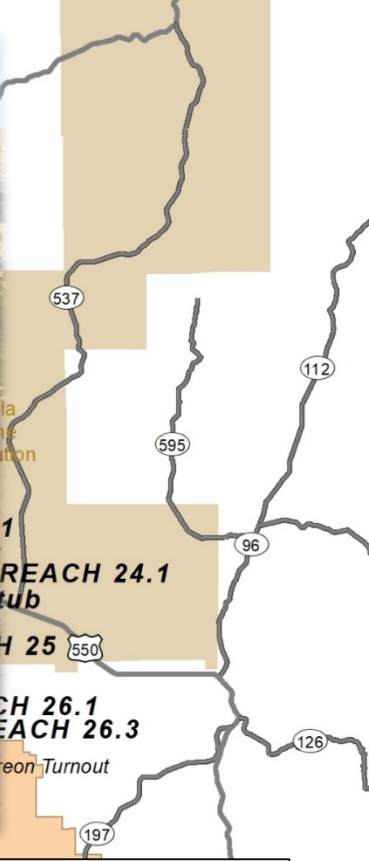

San Juan Generating Station Intake Alternative

